


Twelve days into Beta, the foundation is built and merged.

Every open merge request on GitLab and GitHub landed on main today. The merged build passes all 1,365 automated tests. The numbers below come from the GitLab boards and the git history.

Commits per day on main

149 commits since Sept 21. Sept 22 was the biggest day, with 55.

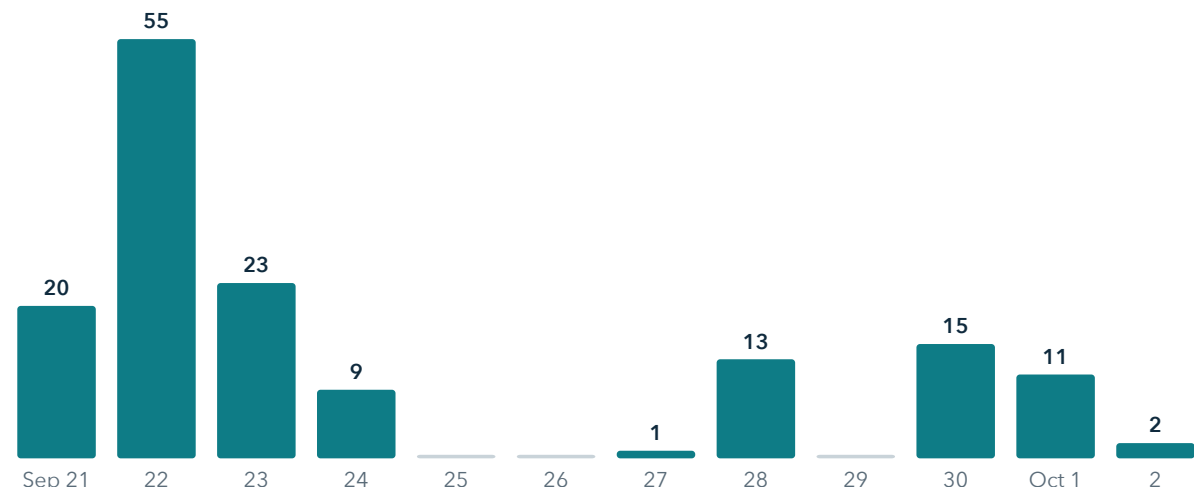

74 of 223

Beta tickets closed or at Evidence, with 122 more ready to pull

39 of 40

merge requests merged on GitLab, 8 of them today

1,365

automated tests passing: 455 frontend, 910 Rust

21 + 23

written decision records and evidence files in the repo

Beta board, all four lanes



Anurup

46 tickets done. Search baseline, capture, memory pipeline

Kunj

14 tickets done. Command contract, tool registry, risk policy

Minh

3 reopen tickets done: QA matrix, unit tests, file paths

Felipe

10 tickets done. Voice system, Touch ID

Anurup

Lead. Search and memory quality, capture, Screen Guide reliability, team operations

46

Beta tickets closed or at Evidence

104

commits, 34,452 code lines changed

68

issues closed all time

Beta tickets assigned: 83



■ Closed **44** ■ At Evidence **2** ■ Doing **3**

■ Ready **34**

What shipped

Search has a measured baseline.

VS-01 recorded Recall@5 0.955 and MRR@10 0.909 for Search, and 1.000 for Ask, on a 20-record knowledge-worker week. Every later search change can now be judged against it.

One memory followed through the real pipeline.

VS-27 records a single memory from capture to result with event-backed evidence, and the six-journey baseline is staged behind it.

Capture became measurable and safer.

ScreenCaptureKit one-shot capture, perceptual-hash dedupe with loop detection, per-stage p50 and p95 timings, and a Privacy Proof screen showing what was skipped and why.

The memory pipeline was audited and covered.

MEM-01 to MEM-11: dead and duplicate code traced, finalization invariants under test, storage indexes, replay sessions with gold stories.

Screen Guide is steadier on Retina displays.

Capture handoff and Retina OCR fixes landed this week, plus an explicit private mode. Full-screen stabilization (GS-15) is in progress.

The team runs on a board.

GitLab labels, weekly milestones, issue and MR templates, TEAM.md, the demo script, and the agent-switch protocol all came from OPS-01 to OPS-12.

Next

Finish Screen Guide diagnostics (GS-15, GS-17), prove activity traces follow real process boundaries (PX-07), and run the six-journey human and agent baseline (VS-28).

Kunj

Command surface, agent, Screen Guide
delivery, release engineering

26

commits, 15,154 code lines changed

14

Beta tickets closed or at Evidence

6

merge requests merged

Beta tickets assigned: 45



■ Closed **3** ■ At Evidence **11** ■ Ready **31**

What shipped

The command bar has a contract.

GS-01 wrote the command-surface contract and amended ADR-014; PD-06 and ADR-022 define what the bar may do this semester.

One typed tool registry.

GS-03 gives every command a typed definition, so voice, the command bar and MCP all call the same tools.

One risk policy for every action.

GS-11 applies the same policy to the command bar, voice and MCP. It is merged to main and now at Evidence on the board.

FNDR can listen at the notch and act on the Mac (FEA-11).

The notch HUD takes spoken requests, and Do mode lets FNDR narrate and operate the Mac with an approval prompt on every action.

Screen Guide shipped natively.

Native delivery, a fixed-state status item, safe local voice input, and privacy-bounded filename lookup (FEA-07 to FEA-10).

The Agent page is one chat (FEA-12).

History, memory context, ChatGPT sign-in, and Hermes back as a model provider.

Releases open, and CI tells the truth (FEA-13, FEA-14).

The release pipeline now produces a DMG people can open. Two hidden Rust test failures, search latency budgets and a dependency bump were fixed so CI stops blocking the team.

Next

Connect Search voice to the command system so Felipe can finish the last Search voice work. This is the one dependency between the two lanes.

Minh

Reopen, embeddings, capture reliability

3

reopen tickets closed or at Evidence (RE-01, RE-02, RE-03)

11

merge requests merged all time

10

issues closed all time

Beta tickets assigned: 32



■ Closed **1** ■ At Evidence **2** ■ Ready **29**

What shipped

Reopen has a QA matrix and unit tests.

RE-01 built the matrix of reopen scenarios on today's build. RE-02 unit-tests how reopen targets are built and resolved, before any rule changes.

Reopen now keeps real file paths.

RE-03 stores native document paths so a memory can take you back to the actual file. It merged today after a conflict with the Screen Guide focus fix was resolved.

Capture runs on its own thread.

The capture pipeline moved to a dedicated thread with a larger stack, and IOKit pauses capture when the keyboard and mouse go idle.

Embedding work shipped earlier in the semester.

BGE v5 reindexing in bounded batches, a fix for BGE query chunk search, and the semantic ranking system for ordering results.

Next

Move the embedding model choice to measurement (VS-17), then use RE-03 paths to lift exact reopen coverage, which the vault baseline puts at 10.3% today.

Felipe

Voice, onboarding, product decisions

10

Beta tickets closed or at Evidence

7

merge requests landed today, in stack order

6

voice entry points inventoried, converging on one control

Beta tickets assigned: 38



■ Closed **4** ■ At Evidence **6** ■ Ready **28**

What shipped

The voice system is built.

Contract (VO-02), native speech helper (VO-03), and a Rust session manager (VO-04) that streams events to the UI.

Permissions and Touch ID work.

Speech and microphone permissions (VO-05). Touch ID now uses a compiled helper, so the app no longer needs the Swift compiler at runtime (OB-02).

One shared voice control for the whole app.

VO-06 built it to replace the separate voice paths. Home now uses it for normal voice input (VO-07), and Search is next.

Voice was measured before it was changed.

VO-01 inventoried every entry point and recorded smoke baselines for Home and Screen Guide.

The product decisions are written down.

PD-15 fixes the five destinations and Labs (ADR-023). PD-16 sets how voice behaves.

Search bar voice is in progress, per Felipe.

Transcription appears asynchronously and nothing searches until the arrow or Enter is used. This is not on main yet.

Next

Wire Search voice commands into Kunj's command system, then finish the last Search voice work. Blocked only on that connection.
